

IL-SEZ/HYD/FAC/EC COMP REPORT/291122

Nov 29, 2022

Deputy Director General of Forests(C)
Ministry of Env., Forest and Climate Change,
Integrated Regional Office,
Hyderabad 3rd Floor, Room No. 309,
Aranya Bhavan, Opp. RBI, Saifabad-500004,
Hyderabad, Telangana.

Dear Sir/Madam,

Sub: Submission of Six-Monthly Compliance Report of EC Conditions-April 2022 to September 2022- M/s. Infosys Limited (IT SEZ Project), Survey Nos, 50 (part) 51, 54, 49, 44 & 45 (part), 41 (part), 36 (part), at Pocharam village, Ghatkesar Mandal, Medchal – Malkajgiri District, 500088 - Reg.

Ref: Environmental Clearance of proposed expansion at Infosys Limited Pocharam SEZ campus vide Order No. SEIAA/TS/OL/MDCL-267/2019-373 dated 09.04.2021

We are pleased to inform the regional office that we have obtained the Environmental Clearance for the proposed expansion of Infosys Limited Pocharam SEZ Campus vide reference cited. We are herewith submitting the Six-Monthly EC Compliance report for the period of April 2022 to September 2022

Thanking you,

Yours sincerely,
for Infosys Limited



Authorized Signatory

Encl: Compliance Details

INFOSYS LIMITED

SEZ Survey No. 41 (pt) 50 (pt)
Pocharam Village
Singapore Township PO
Ghatkesar Mandal
Malkajgiri – Medchal District
Hyderabad 500 088, India
T 91 40 4060 0000
F 91 40 6634 1356

Corporate Office:
CIN: L85110KA1981PLC013115
44, Infosys Avenue
Electronics City, Hosur Road
Bengaluru 560 100, India
T 91 80 2852 0261
F 91 80 2852 0362
askus@infosys.com
www.infosys.com

COMPLIANCE OF ENVIRONMENTAL CLEARANCE CONDITIONS



FOR THE PERIOD: APRIL 2022 TO SEPTEMBER 22

Ref: Environmental Clearance for Expansion of Pocharam Campus

Order No. SEIAA/TS/OL/MDCL-267/2019-373 dated 09.04.2021

Submitted by

Infosys[®]
POWERED BY INTELLECT
DRIVEN BY VALUES

Infosys Limited (IT SEZ Project)

44 & 45(part), 48, 49, 50(part), 51, 54, 36 (part) and 41 (part)
Pocharam (V), Ghatkesar (M), Medchal Malkajgiri - District
TELANGANA.

Compliance Report

Note: During the current assessment period there is no construction activity being carried out. Hence submitting the compliance report on operational phase, General Conditions, and construction Phase wherever applicable only.

PART A: Specific Conditions

| S.No | EC conditions | Compliance status |
|-------|---|--|
| (i) | The project proponent shall provide for adequate fire safety measures and equipment as per National Building Code/required by Fire Services Act of the State and instructions issued by the local Authority/Directorate of fire, from time to time. Further, the project proponent shall take necessary permission/NOC regarding fire safety from Competent Authority as required. | We have obtained Fire NOC for existing buildings (7 SDBs, ECC- G+11, MLCP-G+5). We will obtain the FIRE NOC for proposed buildings from Telangana State Disaster Response and Fire Services Department, Govt of Telangana. |
| (ii) | The project proponent shall obtain all necessary clearance/permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws. | All necessary clearance/permissions obtained for existing buildings. All necessary clearance/permissions will be obtained for proposed buildings. |
| (iii) | The Consent for Operation (CFO)/Occupancy Certificate shall be issued only after getting necessary permission for required water supply from HMWSSB/concerned authority. | Necessary approvals from HMWSSEB/concerned have been obtained for existing buildings. Necessary approvals from HMWSSEB/ concerned will be obtained for proposed expansion. |
| (iv) | The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated wastewater being used for flushing in terms of fecal coliform and other pathogenic bacteria. | We have established a monitoring plan for the existing project to monitor the treated wastewater in terms of fecal coliform and other pathogenic bacteria. Currently treated water is sufficient for use in landscaping and HVAC applications. The monitoring plan will be applied even to the proposed expansion post commencement of operation. |
| (v) | The project proponents would commission a third-party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing and quality of water being supplied through spray faucets attached to toilets seats. | Complied for existing project. We will engage a third-party study on the implementation of wastewater generation, treatment and utilization for the proposed expansion. |
| (vi) | The local bye-law provisions on rainwater harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per Ministry of Urban Development Model Building Byelaws, 2016. The number of rainwater harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines. | We have implemented Rainwater harvesting scheme in the existing project in conformance to local bye - law. Rainwater harvesting system will be implemented in the proposed expansion as per the geography / topography of the ground in line with bye - law. |

| | | |
|--------|--|--|
| (vii) | Rainwater harvesting for roof run-off shall be implemented. Before recharging pre-treatment must be done to remove suspended matter, oil and grease. A sump may also be constructed along with Rainwater harvesting pits to save water. | Rainwater harvesting for roof run-off with necessary treatment facilities have been implemented in the existing project. Rainwater harvesting for roof run-off with necessary treatment facilities will be implemented for the proposed project. |
| (viii) | Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. Designated area shall be provided for solid waste management within the premises which will include area for segregation, composting. The inert waste from project will be sent to dumping site. | In the existing project we have provided separate bins for collection of wet and dry waste. Designated area is provided for segregation and composting. Wet garbage is treated in the Organic Waste Converter and biogas plants and inert waste if any will be disposed as appropriately. For proposed expansion we will implement the separate bins for wet and dry waste. The wet waste will be treated in the existing Organic Waste Converter and biogas plants and inert waste if any will be disposed as appropriately. |
| (ix) | Traffic congestion near the entry and exit points from the roads adjoining the proposed project site must be avoided. Parking should be fully internalized, and no public space should be utilized. | We have provided adequate parking and implemented a Security system which controls the exit and entry of vehicles in the existing project. Provision for adequate parking in the expansion phase is planned and no public spaces will be used for parking. |
| (x) | The company shall draw up and implement corporate social responsibility plan as per the Company's Act of 2013. | CSR activities are implemented and carried out as appropriate. |
| (xi) | The proponent shall earmark funds under Corporate Environment Responsibility (CER) for the activities such as waste Management, Solar Street Lights, Drinking Water, Health Camps, Rainwater harvesting, Training & Education and Avenue Plantation etc. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent. | Environmental management programmes exist covering Solar Street Lights, Drinking Water, Health Camps, Rainwater harvesting, Training & Education and Avenue Plantation etc. The same will be implemented for the proposed expansion. |

B Standard Conditions: -

I. Statutory Compliance:

| S.No | EC conditions | Compliance status |
|------|---|---|
| i | The project proponent shall obtain all necessary clearance/permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws. | All necessary clearance/permissions obtained from relevant agencies for existing buildings. All necessary clearance/permissions will be obtained before commencement of work for proposed buildings. |

| | | |
|------|---|---|
| ii | <p>The proponent shall not discharge any waste water outside the premises until their project's outlet is connected to public sewer line and till such time they will reuse 100% of treated waste water within the project premises; confirm to the WALTA Act and the water consumption shall be as per permissions granted by the Concerned Authorities; confirm to the provisions laid under the Real Estate (Regulation & Development) Act, 2016 issued by the Ministry of Law & Justice, GoI & its subsequent amendments (if any); adopt green building concepts and use renewable energy by adopting Energy Conservation practices, Energy efficient practices & Energy audit practices, etc.,</p> | <p>For existing project, we have provided Sewage Treatment Plant for treating the wastewater. We are in compliance with the applicable legislations including WALTA Act Real Estate (Regulation & Development) Act, 2016 issued by the Ministry of Law & Justice, GoI & its subsequent amendments (if any).</p> <p>The treated wastewater from the existing project is used for greenbelt and HVAC Makeup. We have implemented 1.124 MWhr Roof top solar power and 6.63 MWhr of ground mounted Solar Power Plant.</p> <p>The existing buildings are LEED and GRIHA five star Certified</p> <p>Similar facilities for water and energy conservation are planned in the proposed expansion.</p> |
| iii | <p>The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc. As per National Building Code including protection measures from lightning etc.</p> | <p>Approval from the competent authority (M/s. TRC - structural consultant) is obtained for structural safety of all existing buildings. All the existing buildings are designed and constructed as per NBC guidelines.</p> <p>Approval from the Competent Authority will be obtained for structural safety for proposed buildings. Proposed construction will be designed as per NBC guidelines.</p> |
| iv | <p>The project proponent shall obtain forest clearance under the provisions of Forest (Conservation) Act, 1980, in case of the diversion of forest land for no-forest purpose involved in the project.</p> | <p>Not Applicable since there is no forest land involved in the existing and as well as proposed project.</p> |
| v | <p>The project proponent shall obtain the necessary permission for drawl of ground water / surface water required for the project from the competent authority.</p> | <p>We procure water mainly from municipal sources (Hyderabad Metropolitan Water Supply and Sewerage Board) additionally, we source water for our landscaping requirements through 4 of the 5 existing borewells for which we have the permission from CGWA.</p> |
| vi | <p>A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project should be obtained.</p> | <p>We have obtained necessary approvals from TSPDCL/CEIG-TS for our all-existing buildings.</p> <p>We will obtain necessary approvals from TSPDCL/CEIG-TS for proposed buildings.</p> |
| vii | <p>All other statutory clearances such as approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department shall be obtained, as applicable, by project proponents from the respective competent authorities.</p> | <p>All statutory clearances obtained for the existing buildings.</p> <p>All statutory clearances will be obtained for proposed buildings.</p> |
| viii | <p>The provisions of the Solid Waste Management Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste Management Rules, 2016, shall be followed.</p> | <p>We are in compliance with the requirements of the Solid Waste Management Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste Management Rules, 2016, shall be followed.</p> <p>And shall ensure the same for the proposed expansion project as well.</p> |

| | | |
|----|--|---------------|
| ix | The project proponent shall follow the ECBC/ECBC-R prescribed by Bureau of Energy Efficiency, Ministry of Power strictly | Yes, ensured. |
|----|--|---------------|

II. Air quality monitoring and preservation:

| S.No | EC conditions | Compliance status |
|------|--|---|
| i | Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory Implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with. | Dust mitigation measures to control fugitive dust during construction will be implemented |
| ii | A management plan shall be drawn up and implemented to contain the current exceedance in ambient air quality at the site. | Noted. There is no exceedance in ambient air quality due to the extensive development of greenbelt. In fact, the greenbelt is the largest absorber of CO ₂ in the area. Regular monitoring of environmental parameters is being carried out in the existing project. Similar monitoring of environmental parameters will be implemented in the proposed expansion. Copy of the Report is attached as Annexure- 1 . |
| iii | The project proponent shall install system to carryout Ambient Air Quality monitoring for common/criterion parameters relevant to the main pollutants released (e.g. PM ₁₀ and PM _{2.5}) covering upwind and downwind directions during the construction period. | We are carrying out Ambient Air Quality monitoring in all prominent locations of the existing project. We will carryout Ambient Air Quality monitoring in all prominent locations of the proposed project. |
| iv | Diesel power generating sets proposed as source of backup power should be of enclosed type and confirm to rules made under the Environment (Protection) Act, 1986. The height of stack of DG sets should be equal to the height needed for the combined capacity of all proposed DG sets. Use of low sulphur diesel. The location of the DG sets may be decided within consultation with State Pollution Control Board and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms. | We have installed a DG sets as a backup for our operations and have provided stacks of adequate height for dispersion in line with Environment (Protection) Act. We will install DG sets as a backup for proposed buildings operations and will provided stacks of adequate height for dispersion in line with Environment (Protection) Act. |
| v | Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust/wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murrum and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site. | Appropriate barricading will be ensured. Sprinkling of water and other Measures to prevent emitting of dust, smoke and other pollutants will be ensured at site. Appropriate measures will be taken during material transportation for construction. |
| vi | Sand, murrum, loose soil cement, stored on site shall be covered adequately so as to prevent dust pollution. | Noted. Will be complied. |
| vii | Wet jet shall be provided for grinding and stone cutting. | Noted. Will be complied. |
| viii | Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust. | Noted. Will be complied. |

| | | |
|----|---|--|
| ix | All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Management Rules 2016. | Noted. The construction waste (surplus if any) will be sent to the Construction and Demolition Waste facility at Jeedimetla or Fathulgude (Nagol). |
| x | For indoor air quality the ventilation provisions as per National Building Code of India. | The Indoor air quality is being monitored in the existing buildings and the same will be implemented in the proposed expansion. |

III. Water quality monitoring and preservation:

| S.No | EC conditions | Compliance status |
|------|---|--|
| i | The natural drain system should be maintained for ensure unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest rainwater. | Infosys has already implemented a storm water management plan and rainwater harvesting facilities in the Project site. The natural drain passing through the project site has been strengthened, check dams built and rainwater harvesting lakes have been constructed to store the water. Excess water is discharged into the natural drain. This has helped in improving the ground water table of the surrounding villages and habitations. |
| ii | Buildings shall be designed to follow the natural topography as much as possible. Minimum cutting and filling should be done. | Infosys as a policy has not levelled the project site area to build the existing project buildings. This has been done to protect the natural topography of the project site. Minimum cut and fill was done and confined to the buildings only. Similar practice will be followed for the expansion project. |
| iii | The quantity of freshwater usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. | Individual meters provided to record the usage of fresh water and treated wastewater in the existing project. Individual meters will be provided to record the usage of fresh water and treated wastewater for the expansion project. |
| iv | A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users. | The potable water will be supplied by HMWSSB. And a contract on the same line exists. |
| v | Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing, landscape irrigation, car washing, thermal cooling, conditioning etc., shall be done. | Dual plumbing system for fresh water and other for supply of recycled water have been implemented in the existing project. Dual plumbing system for fresh water and other for supply of recycled water will be implemented for the expansion project. |
| vi | Use of water saving devices/fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc. for water conservation shall be incorporated in the building plan. | Taps are provided with pressure reducing valves and flow restrictors for water saving. Sensor controlled urinals are also provided in the existing project. Similar water conservation measures will be implemented in the proposed expansion project. |

| | | |
|------|--|--|
| vii | Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done. | Dual plumbing system is established in existing project. The treated sewage is used for Landscape and HVAC applications. Dual plumbing system will be established for the proposed expansion. The treated sewage will be used for Landscape and HVAC applications. |
| viii | Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred. | Implemented for the existing project. Will be implemented for the proposed expansion. |
| ix | A rainwater harvesting plan needs to be designed where the recharge bores of minimum on recharge bore per 5,000 square meters of built-up area and storage capacity of minimum one day of total freshwater requirement shall be provided. In areas where ground water recharge is not feasible, the rainwater should be harvested and stored for reuse. The ground water shall not be withdrawn without approval from the Competent Authority. | Noted. Rainwater harvesting has already been implemented for the entire campus. Eight Rainwater harvesting lakes have been constructed and maintained. However, Roof top rainwater harvesting system will be planned in the proposed expansion and integrated with the existing Rainwater harvesting lakes. Photographs are given as Annexure-2 . |
| x | All recharges should be limited to shallow aquifer. | Ensured. |
| xi | Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken form the CGWA for any ground water abstraction or dewatering. | We source water for our landscaping requirements through 4 of the 5 existing borewells for which we have the permission from CGWA |
| xii | No sewage or untreated effluent water would be discharged through storm water drains. | Dedicated Sewage Treatment Plant is provided in existing project. Separate Sewage Treatment Plant will be provided for the proposed project. |
| xiii | Storm water control and its re-use shall be as per CGWD and BIS standards for various applications. | An efficient storm water management plan has been already implemented. Rainwater collected is being reused for various applications after treatment in order to reduce freshwater consumption. In addition to above, storm water drains are routed to lakes of capacity 10 crore liters towards ground water recharge. |
| xiv | The installation of the additional Sewage Treatment Plant (STPs) of capacity – 1100 KLD & 900 KLD should be certified by an independent expert and a report in this regard should be submitted to the SEIAA before the project is commissioned for operation. Discharge of treated wastewater shall conform to the standards stipulated under Schedule-6 of Environment (Protection) Act, 1986 and its amendments thereof. Sewage Treatment Plant should be monitored on a regular basis. No wastewater shall be discharged outside the premises. The excess treated wastewater, if any, is to be reused within the premises ie., discharged into an artificial pond within the premises and can be utilized for recreational purpose. The proponent shall adopt dual plumbing system for reuse of treated wastewater and also take necessary water conservation measure in the project. | Currently there are three STPs in the existing project as given below: <ul style="list-style-type: none"> a) MBR: 1100 KLD b) Conventional Activated Sludge process- 400 KLD (Emergency Standby) c) SBR: 180 KLD (Emergency Standby) The average wastewater at STP Inlet is given below: 2018-2019 – 429 kld 2019-2020 – 564 kld 2020-2021 – 293 kld It may be observed from the above data that the average load on STPs is in the range of 400 – 575 KLD prior to COVID-19 and has further reduced during COVID-19 lockdown to about 300 kld. The current load is about 200 KLD due to Work from Home (WFH) policy implementation. Considering the above facts, INFOSYS is of the opinion to |

| | | |
|----|--|---|
| | | <p>postpone the implementation of the proposed STPs of 1100 kld and 900 kld since adequate existing capacity of about 1680 kld is available. INFOSYS will review the operation of the Campus during FY 2022-23 and if required will upgrade the existing STPs to cater to the additional load of SDB-7.</p> <p>The test report of Analyses of Treated wastewater is enclosed as Annexure -3.</p> |
| xv | <p>Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from Solid waste processing plant & STP.</p> | <p>We have established a monitoring plan for the existing project to monitor the treated wastewater. Necessary measures like Odour control system and Solar sludge drying bed established to mitigate the Odour problem.</p> <p>The monitoring plan for treated water and Odour control system for STP and Solid Waste processing plant will be established to the proposed expansion post commencement of operation.</p> |

IV. Noise monitoring and prevention:

| S.No | EC conditions | Compliance status |
|------|---|---|
| i | <p>Ambient noise levels shall conform to residential area/commercial area/industrial area/silence zone both during day and night as per Noise Pollution (Control and regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be periodically monitored during construction phase. Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB/SPCB.</p> | <p>Ambient noise levels for the existing project is inline with the Noise Pollution (Control and Regulation) Rules, 2000.</p> <p>Ambient noise will be monitoring during construction of the expansion project. Necessary measures will be taken to reduce ambient air and noise levels during construction phase.</p> <p>Copy of the report is enclosed as Annexure-4</p> |
| ii | <p>Noise level survey shall be carried as per the prescribed guidelines and report in this regard shall be submitted to Regional Officer of the Ministry as a part of six-monthly compliance report.</p> | <p>Ambient noise levels for the existing project are in line with the Noise Pollution (Control and Regulation) Rules, 2000.</p> <p>Ambient noise will be monitoring during construction of the expansion project. Necessary measures will be taken to reduce ambient air and noise levels during construction phase.</p> |
| iii | <p>Acoustic enclosures for DG sets, noise barriers from ground-run bays, ear plugs for operating personnel shall be implemented as mitigation measures for noise impact due to ground sources.</p> | <p>The DG sets will be CPCB type certified conforming to noise and emission standards. Necessary arrangements have been implemented for mitigating noise in the existing project.</p> <p>Necessary arrangements will be implemented for DG sets to for mitigating noise.</p> |

V. Energy Conservation measures:

| S.No | EC conditions | Compliance status |
|------|--|---|
| i | <p>Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the state ECBC.</p> | <p>All the existing buildings are designed as per ECBC of Bureau of Energy Efficiency. and all existing buildings are certified by LEED/GRIHA.</p> <p>Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency will be ensured for proposed expansion.</p> <p>The IGBC certificate is enclosed as Annexure-5.</p> |

| | | |
|------|---|---|
| ii | Outdoor and common area lighting shall be LED. Proposed energy saving measures would save about 15% of power. | We have provided LED lighting in the outdoor and common areas of the existing project. And similar type of Energy conservation measures will be implemented in the proposed project. |
| iii | Application of solar energy should be incorporated for illumination of common areas, lighting for gardens and street lighting in addition to provision for solar water heating. A hybrid systems or fully solar system for a portion of the apartments should be provided. | Already roof top solar system and ground based solar system have been implemented in the existing project. Similar roof top solar system will be implemented for the proposed expansion. |
| iv | Opaque wall should meet prescriptive requirement as per Energy Conservation Building Code which proposed to be mandatory for all air-conditioned spaces while it is aspirational for non-air-conditioned spaces by use of appropriate thermal insulation material to fulfil requirement. | The Air conditioning system of the buildings will be designed as ASHRAE Standards keeping in mind the energy conservation measures. For non-air-conditioned spaces appropriate material and insulation will be used to fulfill requirement. |
| v | Use of glass may be reduced by up to 40% to reduce the electricity consumption and load on air-conditioning. If necessary, high quality double glass with special reflective coating in window is to be used. | Low emissivity glass will be used, and common areas will not be air conditioned but be naturally ventilated. The glass content will be maintained up to 40%. |
| vi | Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration, increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window and roof u-values shall be as per Energy Conservation Building Code (ECBC) specifications. | All these architectural elements have been incorporated in the existing buildings. Similar features will be incorporated for the proposed buildings. |
| vii | Energy conservation measures like installation of CFLs/LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning. | Implemented for the existing project. Will be implemented for the proposed expansion. |
| viii | Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter shall be installed for solar power. Solar water heating shall be provided to meet at least 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws requirement, whichever is higher. | Not applicable since the proposed project is a commercial building project |

VI. Waste Management:

| S.No | EC conditions | Compliance status |
|------|--|---|
| i | A certificate from the competent authority who are handling municipal solid wastes, shall be obtained indicating existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from the project. | The entire organic waste / Food waste generated in the campus is treated inhouse in OWC and biogas plants respectively. The inorganic waste like plastics, corrugated boxes, etc. are disposed to authorized recyclers in adherence to applicable legislations. |
| ii | Any hazardous waste including biomedical waste should be disposed of as per applicable Rules & norms with necessary approvals of the Telangana State Pollution Control Board. | Hazardous waste including Biomedical waste is disposed as per applicable rules and necessary approvals of the TSPCB for the existing project. Hazardous waste including Biomedical waste will be disposed as per applicable rules and necessary approvals of the TSPCB for the proposed expansion. |

| | | |
|------|---|--|
| iii | Disposal of muck during construction phase shall not create any adverse effect on the neighboring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approvals sites with the approval of competent authority. | Debris generated during construction (surplus if any) will be sent to the Construction and Demolition Waste facility at Jeedimetla or Fathulgude (Nagol) with proper safety measures. |
| iv | Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. | Separate wet and dry bins have been provided for segregation of wet and inter materials for the existing project. Separate wet and dry bins will be provided for segregation of wet and inter materials for proposed expansion. |
| v | Organic waste compost / vermiculture pit / Organic waste converter within the premises with a minimum capacity of 0.3 kg / person / day must be installed. | An organic waste converter (2 TPD) and biogas plant (2 TPD) are established in the existing project. |
| vi | All non-biodegradable waste shall be handed over to authorized recyclers for which a written tie up must be done with the authorized recyclers. | All non-biodegradable waste is segregated, stored and disposed to authorized recyclers in line with applicable legislations. |
| vii | Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board. | Hazardous waste generated during construction will be disposed to authorized recyclers in line with applicable legislations for the proposed expansion. |
| viii | Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for a least 20% such as Fly Ash Bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks and other environment friendly materials. | Appropriate eco friendly materials will be used in the proposed expansion. |
| ix | Fly ash materials should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27 th August, 2003 and 25 th January, 2016. | Will be implemented in line with the Fly Ash Notification for the proposed expansion project. |
| x | Any wastes from construction and demolition activities related thereto shall be managed to strictly conform to the Construction and Demolition Waste Management Rules, 2016. | Construction and demolition activities for the proposed expansion will be managed in compliance with Construction and Demolition Waste Management Rules, 2016. |
| xi | Used CLFs, and TFLs should be properly collected and disposed off / sent for recycling as per the prevailing guidelines / rules of the regulatory authority to avoid mercury contamination. | Used CLFs and TFLs is being disposed to TS PCB authorized recyclers for the existing project. Used CLFs and TFLs will be disposed to TS PCB authorized recyclers for the proposed expansion. |

VII. Green Cover:

| S.No | EC conditions | Compliance status |
|------|--|--|
| i | Topsoil should be stripped to a depth of 20 cm from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site. | Topsoil will be preserved separately and utilized for greenbelt development. |

| | | |
|-----|---|---|
| ii | No tree cutting/transplantation has been proposed in the instant project. A minimum of 1 tree for every 80 Sq. m of land be planted and maintained. The existing tree will be counted for this purpose. The landscape planning should include plantation of native species. The species with heavy foliage, board leaves and wide canopy cover are desirable. Water intensive and / or invasive species should be not used for landscaping. | The development is planned in such a way that no trees will be cut. The landscape will include plantation of native species. |
| iii | The green belt design along the periphery of the plot shall achieve attenuation factor conforming to the day and night noise standards prescribed for residential land use by the MoE&F, GOI/CPCB. The open spaces inside the plot should be suitably landscaped and covered with vegetation of indigenous variety. Species of Mosquito repellent & Aromatic plants along with other plants shall also be included for development of greenbelt. During nighttime the noise levels measured at the boundary of the building shall be restricted to the permissible levels to comply with the prevalent regulations. The proponent shall develop and maintain greenbelt with tall growing trees instead of lawns, etc., to maximum extent. The proponent shall also Geotag all the saplings planted. | Greenbelt all along the periphery has been done including open areas within the campus to act as a noise barrier. Campus is landscaped with vegetation of indigenous variety with species consisting of Mosquito repellent & Aromatic plants. Geotagging of trees is in progress. Photographs are attached as Annexure – 6. |
| iv | Green area of at least 10% of the site area shall be developed and maintained. | Noted. Already green area of more than 10 % has been developed |

VIII. Transport:

| S.No | EC conditions | Compliance status |
|------|--|--|
| i | The road system can be designed with these basic criteria. a. Hierarchy of roads with proper segregation of vehicular and pedestrian traffic. b. Proper design of entry and exit points. c. Parking norms as per local regulation. | In the existing project all internal roads have been properly designed and implemented with speed control measures like speed breakers, signboards and traffic warning lights, CCTV cameras. Road systems with required criteria will be implemented in the proposed expansion. |
| ii | Vehicles hired for brining construction material to the site should be in good condition and should have a pollution check certificate and should conform to available air and noise emission standards be operated only during non-peak hours. | Noted and will be implemented during construction. |
| iii | Adequate number of parking spaces shall be provided for visitor vehicles. Rest room facilities should be provided for service population. The proponent shall provide public convenience facilities such as toilets, bathrooms, waiting rooms etc. for the drivers, workers etc. so as to maintain cleanness / hygienic conditions in the surroundings of the project. | We have provided adequate parking facility for visitors and facilities such as toilets, washrooms bathrooms, waiting rooms for drivers, workers were provided in existing project. Adequate parking and hygienic conditions will be provided in the proposed expansion. |

IX. Human health issues:

| S.No | EC conditions | Compliance status |
|------|---|--|
| i | All workers working at the construction site and involved in loading, unloading carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask. | Will ensure that the Construction Contractor will adhere to all safety guidelines and provide Personal Protection Equipment (PPE) to all workers. The Safety Engineer of the Project will regularly monitor the same and ensure adherence. |
| ii | For indoor air quality the ventilation provision as per National Building Code of India. | Noted. The ventilation requirement of buildings will be as per National Building Code. |
| iii | Emergency preparedness plan based on the Hazard identification and Risk Assessment (HIRA) and Disaster Management Plan shall be implemented. | We have an established Emergency preparedness plan based on the Hazard identification and Risk Assessment (HIRA) and Disaster Management Plan in existing project. We will establish Emergency preparedness plan based on the Hazard identification and Risk Assessment (HIRA) and Disaster Management Plan for proposed project. |
| iv | Provision shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project. | We will ensure that the construction contractor will provide the infrastructural facilities like mobile toilets, safe drinking water, medical health care, etc to the labour deployed at site. |
| v | Occupational health surveillance of the workers shall be done on a regular basis. | Noted. |
| vi | A First Aid Room shall be provided in the project both during construction and operations of the project. | Medical facilities are provided with 24/7 service. Medical center available with medical staff (Doctor, Nursing staffs and pharmacy). Tied-up with local hospitals for necessary support in case of requirement. Ambulances are available in the campus for movement in case of emergency. First aid Room with necessary arrangements shall be provided during construction |

X. Corporate Environment Responsibility:

| S.No | EC conditions | Compliance status |
|------|---|--|
| i | The project shall have a well laid down environment policy. The environmental policy should prescribe for standard operating procedures to have proper checks and balances and to bring into focus any infringements / deviation / violation of the environmental conditions. | Environment Policy is framed and is in place for the organization |
| ii | A separate Environmental Cell to monitor the environmental conditions / norms with qualified personnel shall be set up. | An Environmental Management system is established and has been certified as per ISO: 14001:2015 standards. Suitable professionals take care of all respective environmental related aspects. |
| iii | Action plan for implementing EMP and environmental conditions shall be prepared. The year wise funds earmarked for environmental protection measure shall be kept in separate and not to be diverted for any other purpose. Year wise progress of implementation of action plan shall be reported to Ministry / Regional Office along with Six Monthly Compliance Report. | Noted and will be implemented. |

| | | |
|----|---|--|
| iv | The proponent shall strictly follow the OM No. 22-65/217-IA.III dt: 25.02.2021 and implement the commitments made the project proponent as a part of CER contained in EIA/EMP report. | Not Applicable since this OM has been withdrawn by the Ministry vide F.NO 22-65/2017-IA.III dated 30 th September 2020. However, the project proponent will implement CSR activities as per their Corporate Plan. |
|----|---|--|

Part – B. General Conditions:

| S.No | EC conditions | Compliance status |
|------|---|--|
| i | This order is valid for a period of 7 years from the date of issue of this order. | Noted. |
| ii | "Consent for Establishment" (CFE) shall be obtained from Telangana State Pollution Control Board under Air and Water Act before the start of any construction work at site under Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974. | Consent for Establishment is obtained from Telangana State Pollution control board. |
| iii | Consent for Operation (CFO) of the project shall be obtained from the Telangana State Pollution Control Board as required under Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974, after obtaining CFE of the Board, before occupancy. | Consent for Operation will be obtained from Telangana State Pollution Control Board. |
| iv | The proponent shall not carry out any construction activity in the earmarked Open area, green area & Road area of the project, as committed by the project proponent. Any deviation in the proposed earmarked areas shall EC invalid. | No construction activity will be carried out in open area, green area and Road areas of the Project as per the Masterplan submitted in the EIA Report |
| v | The proponent shall: not discharge any waste water outside the premises until their project's outlet is connected to public sewer line and till such time they will reuse 100% of treated waste water within the project premises; conform to the WALTA Act and the water consumption shall be as per permissions granted by the Concerned Authorities; adopt green building concepts and use renewable energy by adopting Energy Conservation practices, Energy efficient practices & Energy audit practices, Develop green area with tall growing tree species, Make provision for Solar cum Wind Energy on Roof etc. | All treated wastewater from the STPs will be utilized for greenbelt development and HVAC Makeup. The buildings will be LEED/GRIHA Certified and comply with ECBC guidelines. Rooftop solar plant will be installed as per feasibility. |
| vi | The environment safeguards contained in the EMP Report should be implemented in letter and spirit. The responsibility of implementation of environmental safeguards rests fully with the proponent ie., M/s. INFOSYS LIMITED (formerly Infosys Technologies Limited) | Noted and will be implemented. |
| vii | All the conditions, liabilities and legal provisions contained in the EC shall be equally applicable to the successor management of the project in the event of the project proponent transferring the ownership, maintenance of management of the project to any other entity. | Noted. |

| | | |
|------|---|--|
| viii | The proponent shall submit half-yearly compliance reports in respect of the terms and conditions stipulated in this order in hard and soft copies to the SEIAA; TSPCB and CCF, Regional office of MOEF&CC, GOI, Hyderabad on 1 st June and 1 st December of each calendar year. | Noted and will be implemented. |
| ix | The proponent shall submit the Environmental Statement for every financial year in FORM-V to the State PCB as prescribed under E(P) Act, 1986, as amended subsequently and will be put on the website of the project. | Noted and will be implemented |
| x | Officials from the TSPCB and Regional Office of MoEF&CC, GoI, Hyderabad who would be monitoring the implementation of environmental safeguards should be given full co-operation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents shall be submitted to the TSPCB and CCF, Regional Office to MoEF&CC, GOI, Hyderabad. | Necessary co-operation is extended, and records are submitted to the PCB Authorities. |
| xi | The proponent should implement the project as per the details mentioned in this order. In the case of any change (s) in the scope of the project, the project would require a fresh appraisal by this SEIAA. No further expansion or modifications in the project shall be carried out without prior approval of the SEIAA, TS. | Noted. Infosys will obtain necessary amendments in case of any changes /modifications in the original proposal for which EC has been obtained. |
| xii | The project proponent shall submit the copies of the environmental clearance to the Head of Local bodies, Panchayats of Municipal Bodies in addition to the relevant offices of the Government who in turn has to display the same for 30 days from the date of receipt. | Not Applicable since the Project is exempt from Public Hearing as per EIA Notification dated 14-09-2006 and its amendments thereof. |
| xiii | The project proponent shall obtain all other statutory clearances, as applicable, from the competent authorities. | Noted and will be implemented. |
| xiv | The project proponent should advertise in at least two local newspapers widely circulated in the region, one of which shall be in the vernacular language informing the project has been accorded environmental clearance and copies of clearance letter are available with the Telangana State Pollution Board. The advertisement should be made within 7days from the day of issue of the clearance letter and a copy of the same should be forwarded to the Regional Office of this Ministry at Hyderabad. | Noted. The Project Proponent had advertised in 2 local Newspapers. The copy of the Advertisements is attached as Annexure - 7 |
| xv | The funds earmarked of environmental protection measures (capital cost: Rs. 5260.0 Lakhs are recurring cost: Rs. 338.58 lakhs/annum) should be kept in separate account and should not be delivered for other purpose. Year wise expenditure should be reported to the SEIA and Ministry's Regional Office located at Hyderabad and TSPCB. | Noted and implemented. |
| xvi | Any appeal against the Environmental Clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010. | Noted |

| | | |
|-------|---|--------|
| xvii | The SEIAA may revoke or suspend the order, if implementation of any of the above conditions is not satisfactory. The SEIAA reverses the right to alter/modify the above conditions or stipulate any further condition in the interest of environment protection. | Noted |
| xviii | Concealing the factual data or failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of Environment (Protection) Act, 1986 without any prior notice. | Noted |
| xix | These stipulations would be enforced among others under provisions of Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and EIA Notification, 2006 and its amendments thereof. | Noted |
| xx | Grant of EC is also subject to Circulars issued under the EIA Notification 2006, which are available on the MOEF website: www.parivesh.nic.in | Noted. |

LIST OF ANNEXURES


| ANNEXURE NUMBER | DESCRIPITON |
|-----------------|--|
| ANNEXURE NO -1 | Copy of Ambient Air Quality Test Reports |
| ANNEXURE NO -2 | Photographs of the Rainwater harvesting lakes/ponds |
| ANNEXURE NO -3 | Copy of the test report for STP treated wastewater quality |
| ANNEXURE NO -4 | Copy of the test Report showing the Ambient Noise level of the Project |
| ANNEXURE NO -5 | Copy of the IGBC Certificate |
| ANNEXURE NO -6 | Photographs of the Greenbelt and Landscaping |
| ANNEXURE NO -7 | The copy of the Advertisements |


WATER HARVESTING SYSTEM

INFOSYS LIMITED

POCHARM



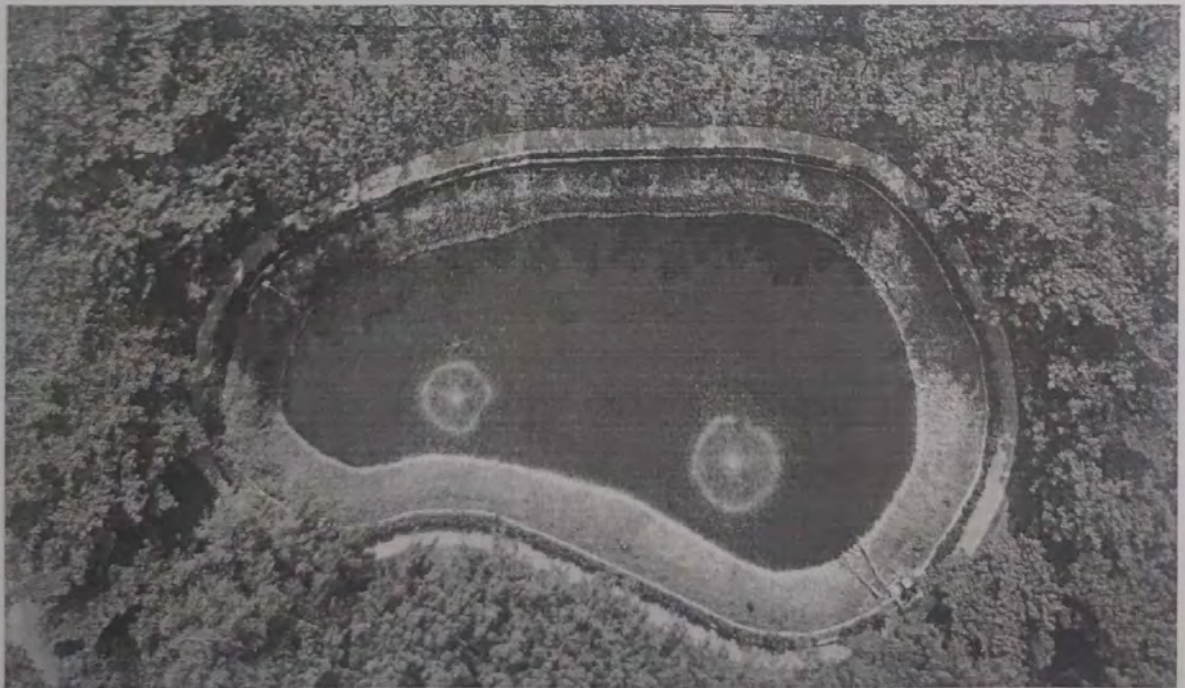

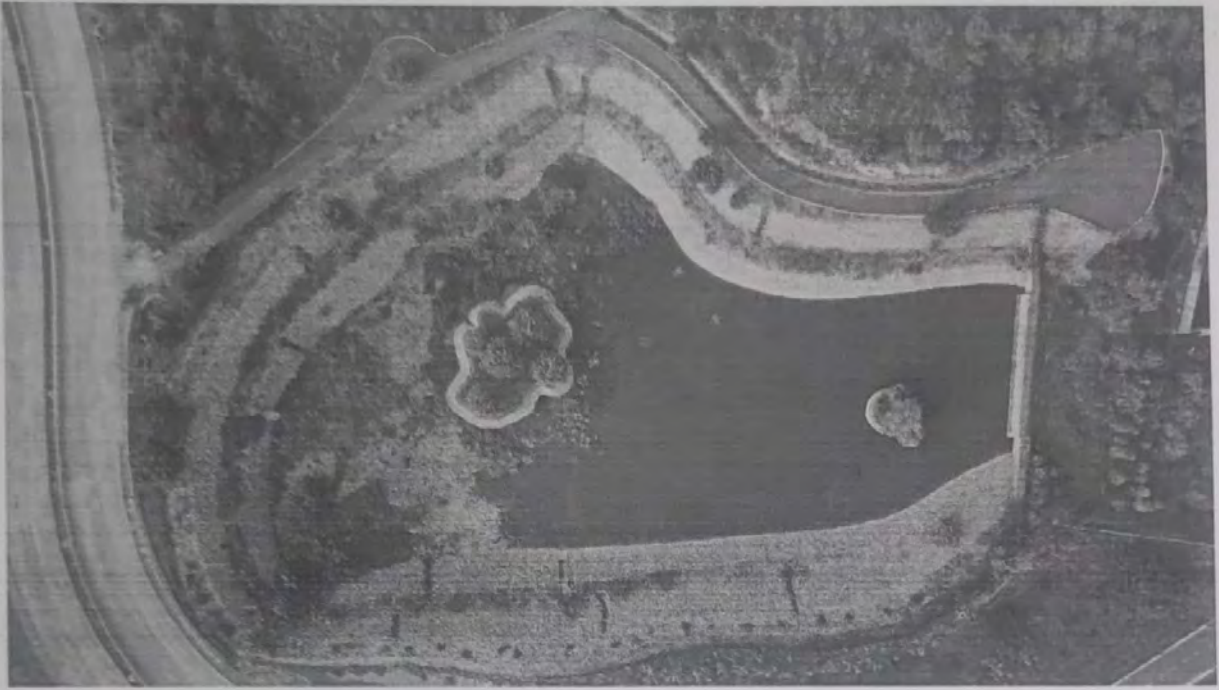

CERTIFICATIONS AND AWARDS




SDB 1, SDB 2 & SDB 3 – LEED
Platinum Certified Buildings
SDB 4 & SDB 5 – GRIHA 5 Star
Certified Buildings

LEED: Leadership in Energy and
Environmental Design

GRIHA : Green Rating for Integrated
Habitat Assessment

SDB-1 Building Certified as LEED Platinum



Indian Green Building Council (IGBC)

hereby certifies that

Software Development Block-1, Infosys SEZ campus
Pocharam, Hyderabad

has successfully achieved the Green Building Standards required for
the following level of certification under the Leadership in Energy and Environment Design
(LEED) India Green Building Rating System


LEED India for New Construction Platinum
April 2012

C N Raghavendran
Chairman, LEED India

Dr Prem C Jain
Chairman, IGBC

Jamsheed N Godrej
Chairman, CII-Godrej GBC

SDB- 2&3 Building Certified as LEED Platinum




Indian Green Building Council (IGBC)


hereby certifies that


**Infosys SDB - 2 & 3
Pocharam, Hyderabad**

*has successfully achieved the Green Building Standards required for
the following level of certification under the Leadership in Energy and Environment Design
(LEED) for India Green Building Rating System*

**LEED India for New Construction Platinum
December 2013**


C N Raghavendran
Chairman, LEED India


Dr Prem C Jain
Chairman, IGBC


S Raghupathy
Executive Director, CII-Godrej GBC

SDB-4 Building Certified as GRIHA 5 Star

INFOSYS SDB-4
HYDERABAD
has been provisionally certified with a
'5 Star'
rating under
GRIHA
(Green Rating for Integrated Habitat Assessment)
The Indigenous Rating System for green buildings in India



An Initiative of
The Ministry of New and Renewable Energy
Government of India
and
The Energy and Resources Institute

SDB-5 Building Certified as GRIHA 5 Star

INFOSYS SDB - 5
HYDERABAD
has been provisionally certified with a
'5 Star'
rating under
GRIHA
(Green Rating for Integrated Habitat Assessment)
The Indigenous Rating System for green buildings in India



An Initiative of
The Ministry of New and Renewable Energy
Government of India
and
The Energy and Resources Institute

SDB-6 Building Certified as LEED Platinum



Thank You

© 2018 Infosys Limited. All Rights Reserved. Infosys believes the information in this document is accurate as of the publication date; such information is subject to change without notice. Infosys acknowledges the proprietary rights of other companies for its trademarks, product names, and such other intellectual property rights mentioned in this document. Except as expressly permitted, neither this document nor any part of it may be reproduced, stored in a retrieval system, or transmitted in any form or by any means, electronic, mechanical, printing, photocopying, recording or otherwise, without the prior permission of Infosys Limited and/or any named intellectual property rights holders under this document.

Infosys® | Building Tomorrow's Enterprise

GREEN BELT

INFOSYS LIMITED

POCHARM













Annexure - 7

PUBLIC NOTICE

M/s. Infosys Limited (Formerly Infosys Technologies Limited) is pleased to inform the general public that it has been accorded Environmental Clearance (Order No. SEIAA/TS/OL/MDCL-267/2019- Dt.: 09.04.2021), by the State Level Environment Impact Assessment Authority (SEIAA) for the proposed expansion. Copies of the clearance letter are available with Telangana State Pollution Control Board and can also be seen at website of the MoEFCC at <http://parvesh.nic.in>.

M/s. INFOSYS LIMITED
(Formerly Infosys Technologies Limited)
Dass Gunkan, Associate Vice President
& Regional Head - Facilities

Published on THE TIMES OF INDIA Hyderabad Edition on 27.05.2021

బ్లాక్‌డేలో పాల్గొన్న విద్యార్థులు : ఎస్‌ఎఫ్‌ఐ

నవతెలంగాణ బ్యూరో - హైదరాబాద్

దేశవ్యాప్తంగా రైతాంగ పోరాటానికి మద్దతుగా బుధవారం నిర్వహించిన బ్లాక్‌డేలో రాష్ట్రవ్యాప్తంగా విద్యార్థులు పాల్గొన్నారని ఎస్‌ఎఫ్‌ఐ రాష్ట్ర అధ్యక్షులు ఆలేషర్ మూర్తి, కార్కడర్లు డి. నాగరాజు తెలిపారు. విద్యార్థుల సెమిస్టర్ ఫీజులను ప్రభుత్వమే చెల్లించాలని బుధవారం ఒక ప్రకటనలో డిమాండ్ చేశారు.

కోలాహ ఉధృతి
సేపల్లూలో ప్రతి
విద్యార్థికి వెలకు
రూ. 7,500
సహాయం
అందించాలని
కోరారు.

బహిరంగ ప్రకటన

ప్రతిపాటిత రిటరన్ కౌతుక్ స్టోర్ లిమిటెడ్ ఎన్‌ఐఎంఐఐ అసోసియేట్ ఆఫీసర్ (NIAA) నీ పద్మావతి అసోసియేట్స్ ప్రైవేట్ లిమిటెడ్ (BEIANTS/OLMDCL/387/2019 - తేదీ 09-04-2021) అధిపతిత్వంలో నాగరాజు ప్రకటించిన మొత్తం బిల్లులను రద్దు చేసే అంశంపై (గతంలో అసోసియేట్ కెటెగోరిస్ లిమిటెడ్) నాగరాజు అసోసియేట్స్ ప్రైవేట్ లిమిటెడ్ కేసు డిమాండ్ వారిని తెలంగాణ రాష్ట్ర అసోసియేట్స్ వేదికంపై వెబ్‌సైట్ పేజీ అందరికీ అందించినా MIBFCC డిమాండ్ నెట్వర్క్ <https://navatelangana.com> వద్ద కూడా సమాచారం.

(మొత్తం బిల్లులను రద్దు చేసే అంశంపై అసోసియేట్ కెటెగోరిస్ లిమిటెడ్) వారి గురించి
అసోసియేట్స్ ప్రైవేట్ లిమిటెడ్ కి సంబంధించిన వివరాలివే.

Published on NAVA TELANGANA
Hyderabad edition on 27.05.2021

సవతిలంగాణ

Thu, 27 May 2021

<https://epaper.navatelangana.com/c/6071>

